



## **Project Schedule**

#### **Project Phases**

- 1. RFQ: 30% Schematic Design-Nov. 2023
- 2. 30% Schematic Design Contract Awarded Feb. 2024
- 3. 30% Schematic Design Submittal Beach House and Access Project June 2024
- 4. 100% Construction Documents Contract Awarded March 12, 2025
  - A. 100% Design Development Estimate May 16
  - B. 100% Design Development Drawings May 30
  - C. 100% CDs Final Sept. 26, 2025
  - D. Permit Submittal Sept. 29, 2025 (Actual Sept. 19, 2025)
  - E. Bid Project Oct. 2, 2025 / Bid Opening Oct. 23, 2025
  - F. GMP Draft to District Nov. 13, 2025 (Comments Nov. 13 Nov. 20, 2025)
  - G. Final GMP Dec. 3, 2025
  - H. GMP Approval by Board of Trustees Dec. 10. 2025
  - I. TRPA/County Approval April 2026
  - J. Construction May 1, 2026

### Design Development Cost Estimate Breakdown

### **Beach House Project**

• Beach House:

• Site Improvements: \$3,102,222

• Restrooms: \$2,626,493

• Kitchen: \$3,463,137

• Bar & Patio: \$990,673

Total \$10,182,525

Alternates:

• Alt #1 – Fire Pits: \$53,283

• Alt #2 – Band Stand: \$54,273

• Alt #3 – Privacy Wall: \$148,368


• Alt #4 - Day Use Lockers: \$16,026

• Alt #5 - RFID Ped. Gate: \$22,943


• Alt #6 – Showers: \$60,268

Total \$255,924

Total Project Cost \$10,438,449

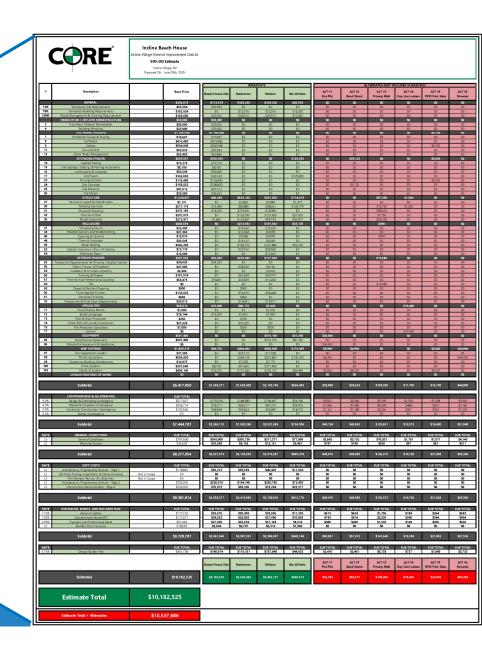

## Add-Alternates

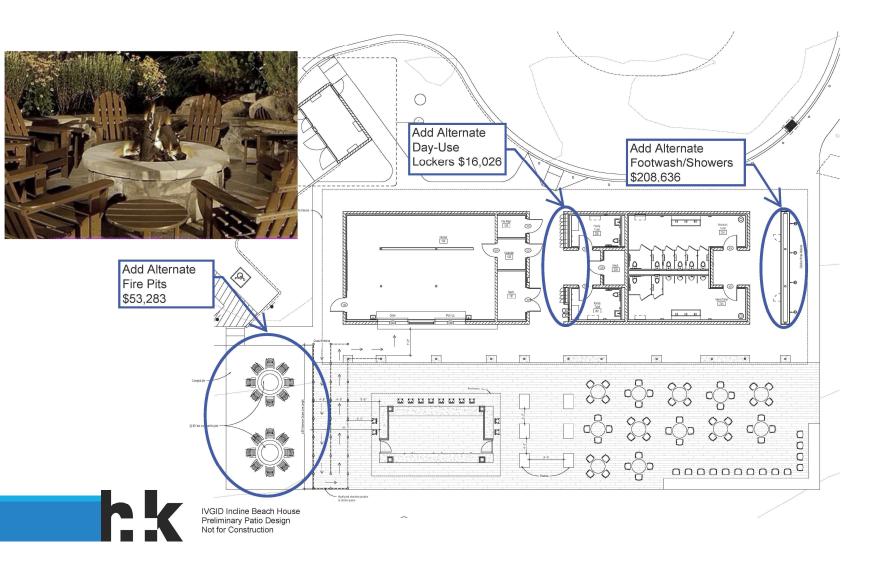



# Add-Alternates

